

FINAL PROGRESS REPORT

Gulf Boulevard Beach Access Improvements

14-092-000-7960

Task 1: Project Design and Bidding

- Provide a brief description of status of the task: not started in progress completed
- Describe major accomplishments for this reporting period (include names of staff working on each task, dates and locations of events/presentations/meetings and dates for milestones/deliverables completed.)

The City developed a request for qualifications to solicit qualified engineering firms for professional services to develop a project design to bid the project in accordance with local and state procurement policy. The City provided the design and contract/bid specifications to the GLO for review prior to the bid solicitation.

- List the deliverable(s)/milestone(s) for the task and provide the date completed/submitted to the GLO.

Deliverable Name	Date Due	Date submitted	Comments
1) Copy of Professional Services Provider Contract	12/31/2013	6/25/2014	
2) Final Project Designs and Specifications	12/31/2013	7/14/2014	
3) Contract Documents/Bid Documents for review	12/31/2013	7/14/2014	

- Were there any problems or obstacles encountered during this reporting period (e.g., delays, remedial action taken, schedule revision). Yes No If yes, please explain:

Task 2: Contractor Selection and Construction

- Provide a brief description of status of the task: not started in progress completed
- Describe major accomplishments for this reporting period (include names of staff working on each task, dates and locations of events/presentations/meetings and dates for milestones/deliverables completed.)

In July 2014, the City held a pre-construction meeting. In September 2014, the project was advertised and bid out. The City selected G & T Paving Company as the construction contractor. In October 2014, the City commenced construction. In February 2015, the City completed improvements to beach access parking and pedestrian safety over six blocks of Gulf Blvd. Safety improvements included the installation of a permanent and designated pedestrian and bike path on the east side of the R.O.W. along with improved parking spaces along the west side which formalized existing parking spaces that were previously grassy areas.

- List the deliverable(s)/milestone(s) for the task and provide the date completed/submitted to the GLO.

Deliverable Name	Date Due	Date submitted	Comments
1) Copy of advertisements, Bid	3/15/2014	10/10/14	

<i>Matrix, and executed construction contract</i>			
<i>2) Photos before, during, and after project completion</i>	<i>3/15/2014</i>	<i>3/16/15</i>	

- Were there any problems or obstacles encountered during this reporting period (e.g., delays, remedial action taken, schedule revision). Yes No If yes, please explain:

Task 3: Project Monitoring and Reporting

- Provide a brief description of status of the task: not started in progress completed
- Describe major accomplishments for this reporting period (include names of staff working on each task, dates and locations of events/presentations/meetings and dates for milestones/deliverables completed.)

Completed project monitoring and reporting.

- List the deliverable(s)/milestone(s) for the task and provide the date completed/submitted to the GLO.

Deliverable Name	Date Due	Date submitted	Comments
<i>Grant Closeout Report</i>	<i>3/31/2015</i>		

Reimbursement requests no.	Date Submitted	Comments
1132104	11/4/14	
11252014	11/25/14	
01072015	1/7/15	
02092015	2/9/2015	
<i>Continue as needed to document invoices submitted</i>		

- Were there any problems or obstacles encountered during this reporting period (e.g., delays, remedial action taken, schedule revision). Yes No If yes, please explain:

CMP Project # 14-092-000-7960

Gulf Blvd Phase 2

CMP Project # 14-092-000-7960

- Beach access parking and pedestrian safety improvements were done over 6 blocks along the Northern most section of Gulf Blvd.
- Block 1 is North of E. Sunset Dr.
- Block 2 is between E. Sunset Dr. and E. Palmetto Dr.
- Block 3 is between E. Palmetto Dr. and E. Parade Dr.
- Block 4 is between E. Parade Dr. and E. Coronado Dr.
- Block 5 is between E. Coronado Dr. and E. Morningside Dr.
- Block 6 is between E. Morningside Dr. and Cora Lee Dr.

Block 1 is North of E. Sunset Dr.



Block 1 is North of E. Sunset Dr. During Construction




The new design includes a cul-de-sac at the end of Gulf Blvd with curb & gutter and raised sidewalk on the East side.

Block 1 is North of E. Sunset Dr. Completed Construction



Block 2 is between E. Sunset Dr. and E. Palmetto Dr.

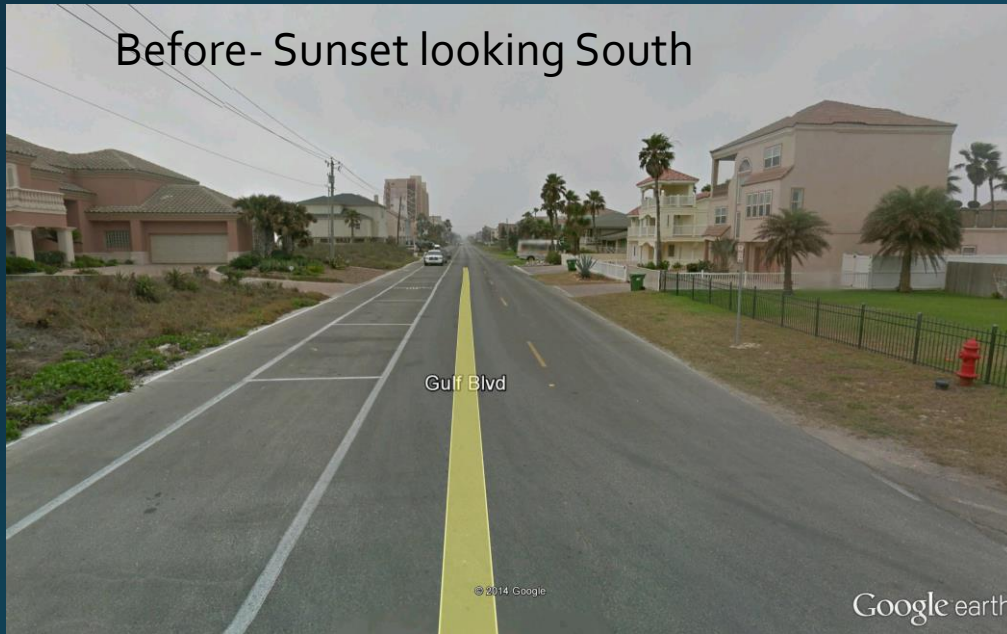


Block 2 is between E. Sunset Dr. and E. Palmetto Dr. During Construction



Block 2 is between E. Sunset Dr. and E. Palmetto Dr. Completed Construction



Block 3 is between E. Palmetto Dr. and E. Parade Dr.

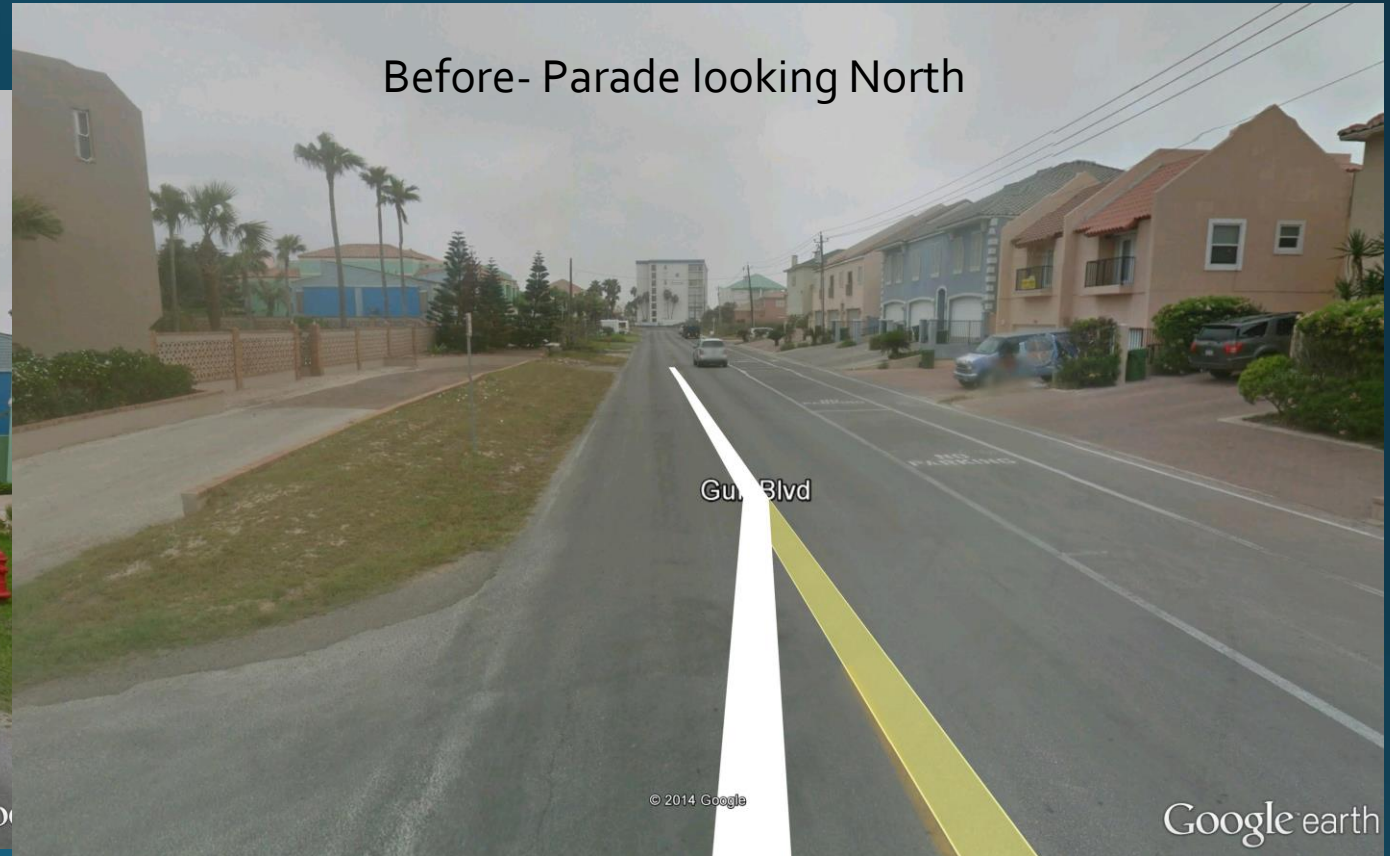


Block 3 is between E. Palmetto Dr. and E. Parade Dr. During Construction



Block 3 is between E. Palmetto Dr. and E. Parade Dr. Completed Construction



Block 4 is between E. Parade Dr. and E. Coronado Dr.

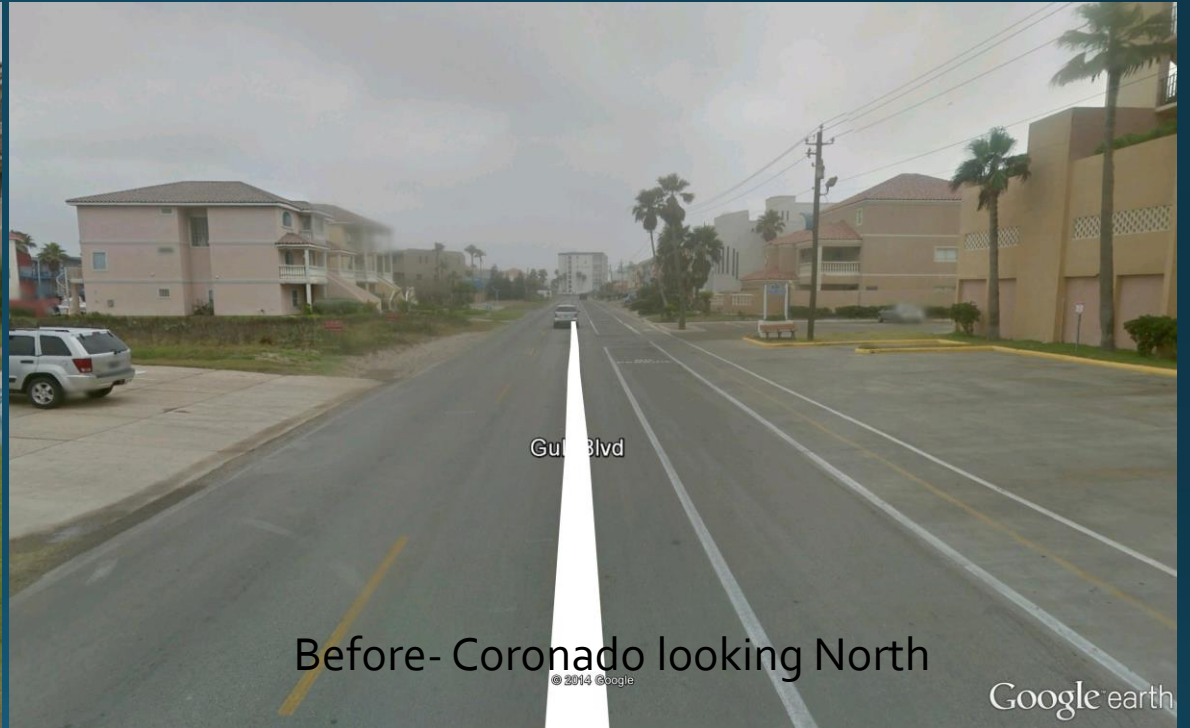


Block 4 is between E. Parade Dr. and E. Coronado Dr. During Construction



Block 4 is between E. Parade Dr. and E. Coronado Dr. Completed Construction



Block 5 is between E. Coronado Dr. and E. Morningside Dr.

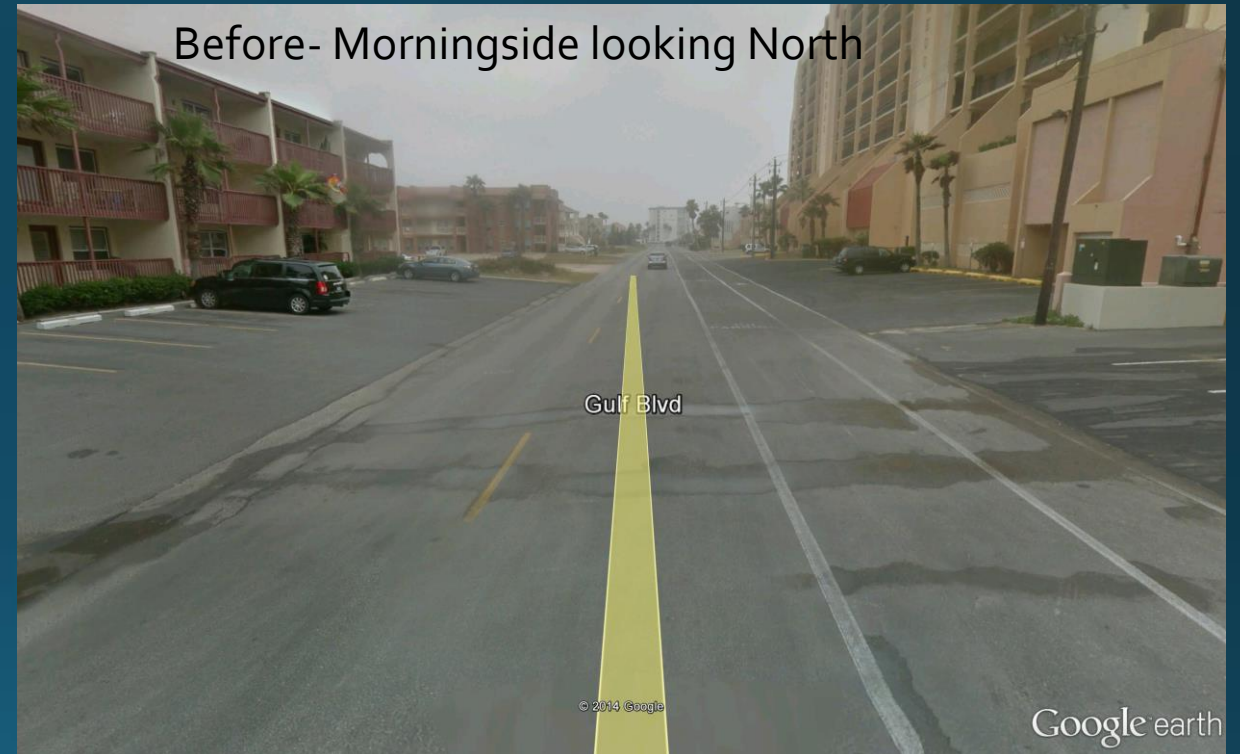

Block 5 is between E. Coronado Dr. and E. Morningside Dr. During Construction



Block 5 is between E. Coronado Dr. and E. Morningside Dr. Completed Construction




Block 6 is between E. Morningside Dr. and Cora Lee Dr.

Before- Morningside looking South



Before- Coralee looking North

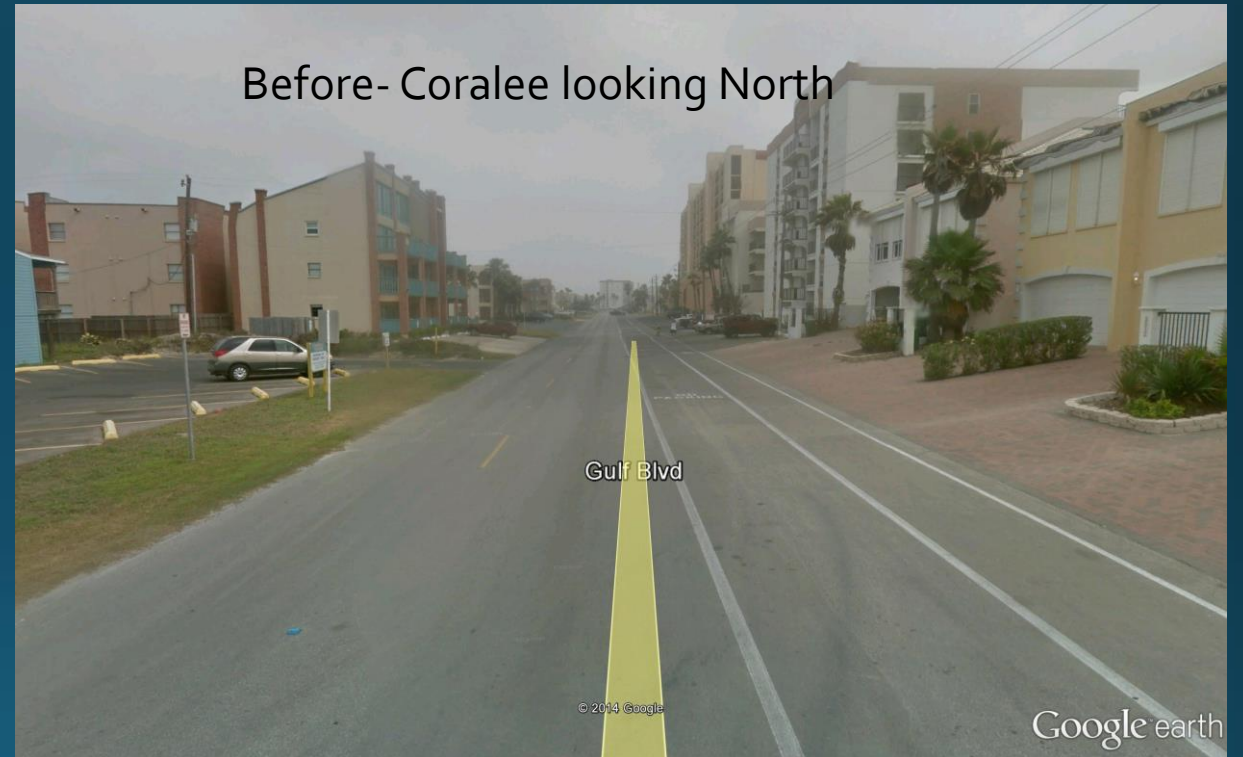

Block 6 is between E. Morningside Dr. and Cora Lee Dr. During



Block 6 is between E. Morningside Dr. and Cora Lee Dr. Completed



Beachgoer Crosswalks

New design will have 2 pedestrian cross walks at every intersection.
All crosswalks have been completed in the project area.

